
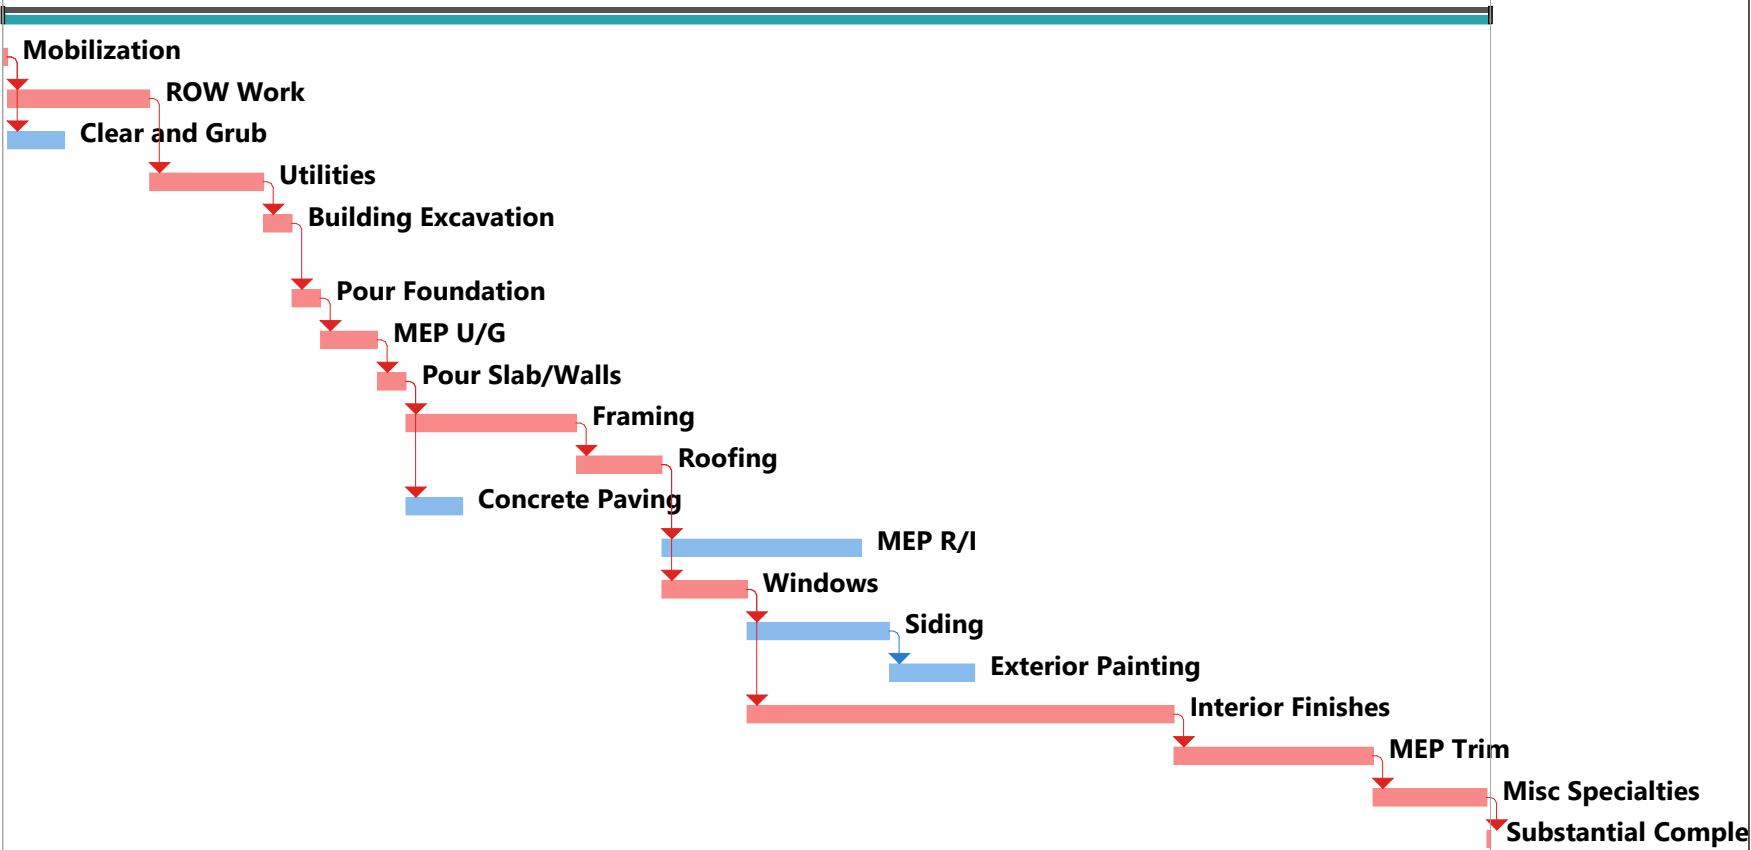



ID		Task Mode	Task Name	Duration	Start	Finish	Aug	Sep	Qtr 4, 2025 Oct	Nov	Dec	Qtr 1, 2026 Jan	Feb	Mar	Qtr 2, 2026 Apr	May	Jun	Qtr 3, 2026 Jul	Aug	Sep	Qtr 4, 2026 Oct	Nov
1			The Talmon	262 days	Mon 9/29/25	Tue 9/29/26																
2			Mobilization	1 day	Mon 9/29/25	Mon 9/29/25																
3			ROW Work	25 days	Tue 9/30/25	Mon 11/3/25																
4			Clear and Grub	10 days	Tue 9/30/25	Mon 10/13/25																
5			Utilities	20 days	Tue 11/4/25	Mon 12/1/25																
6			Building Excavation	5 days	Tue 12/2/25	Mon 12/8/25																
7			Pour Foundation	5 days	Tue 12/9/25	Mon 12/15/25																
8			MEP U/G	10 days	Tue 12/16/25	Mon 12/29/25																
9			Pour Slab/Walls	5 days	Tue 12/30/25	Mon 1/5/26																
10			Framing	30 days	Tue 1/6/26	Mon 2/16/26																
11			Roofing	15 days	Tue 2/17/26	Mon 3/9/26																
12			Concrete Paving	10 days	Tue 1/6/26	Mon 1/19/26																
13			MEP R/I	35 days	Tue 3/10/26	Mon 4/27/26																
14			Windows	15 days	Tue 3/10/26	Mon 3/30/26																
15			Siding	25 days	Tue 3/31/26	Mon 5/4/26																
16			Exterior Painting	15 days	Tue 5/5/26	Mon 5/25/26																
17			Interior Finishes	75 days	Tue 3/31/26	Mon 7/13/26																
18			MEP Trim	35 days	Tue 7/14/26	Mon 8/31/26																
19			Misc Specialties	20 days	Tue 9/1/26	Mon 9/28/26																
20			Substantial Completion	1 day	Tue 9/29/26	Tue 9/29/26																



Project: The Talmon - Town of L Date: Thu 9/25/25	Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
	Split		Inactive Milestone		Manual Summary		Deadline			
	Milestone		Inactive Summary		Start-only		Critical			
	Summary		Manual Task		Finish-only		Critical Split			
	Project Summary		Duration-only		External Tasks		Progress			
